




# TWO WEEK LOOK AHEAD

Project: **Modernising Belconnen High School**  
 Address: **111 Murrarji Street, Hawker, ACT**  
 Date: **12/10/2018 – 26/10/2018**

Note: *The Two Week Look-ahead' provides a general overview of Cockram Construction's scheduled works over the next two weeks. The dates provided are anticipated dates and are subject to change without notification.*

## Belconnen High Directly Impacted Works

The school can be accessed via the gate next to the canteen and the gate at the new main entry which will allow access to the rest of the school.

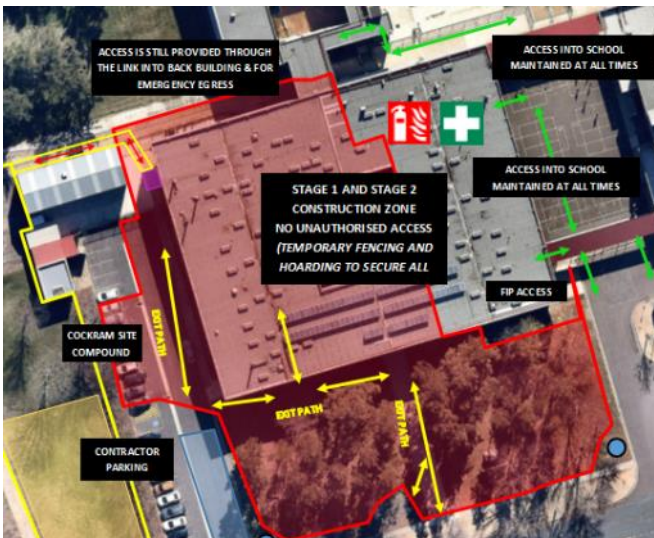

## Works Update 12/10/18 – 26/10/18

With the completion of demolition to the link area a temporary bridge is now installed. Additional airlocks for Stage 1 is now complete with final finishes underway.

Works commenced this week include:

- Installation of structural steel for façade screen
- Concrete pour for overhang slabs
- Concrete pour for new stairs
- Installation of Grease Arrester
- Installation of posts for perimeter fencing

## Services 12/10/18 – 26/10/18

CCA and services contractors are working closely together to coordinate the isolation and relocation of services within Stage 2. Existing services will be managed to ensure that functions required for day-to-day operations within the school are maintained.

Electrical services fit-off is scheduled to commence in the upcoming weeks. Internal hydraulic rough-in works is nearing completion with mechanical works underway.

All services trades are working together with CCA to ensure that any site issues are resolved in a timely manner.

## Off-Site 12/10/18 – 26/10/18

To date, all program critical trades for Stage 2 have been engaged. CCA will be working in collaboration with EDU and consultants to coordinate design elements for Stage 2. CCA continues to work closely with EDU and the School to ensure the project is completed in line with the requirements of the Education Directorate.

## Site Traffic Management 12/10/18 – 26/10/18

Traffic management and Cockram supervision is implemented for all construction traffic. Ongoing Traffic management will continue as per the Temporary Traffic Management Plan and will be used as required for all forthcoming deliveries.

## Site Access 12/10/18 – 26/10/18

**ALL VISITORS MUST REPORT TO THE SITE OFFICE PRIOR TO ENTERING ANY OF THE CONSTRUCTION SITE.**

- All contractors must park within the CCA site compound accessed off Murrarji Street or west of the school.
- All workers must report and sign in at the CCA site compound prior to starting work on site.
- Any persons requiring roof access are to report to CCA prior to works commencing.
- Construction site entry will be from Murrarji Street.
- Security cameras are installed on site to ensure the security of materials and equipment. These will only be recording outside of school hours.

## Important Considerations

1. *Works scheduled above are a guide only and may be subject to change without notice due to a number of unforeseen events or circumstances. Cockram Construction will employ all reasonable measures to reduce disturbance to the school and neighboring residents.*
2. *Working times will vary and should be expected between the hours of 6.00am – 6.00pm Monday to Saturday.*
3. *Heavy vehicles will be entering the site via Murrarji Street for the duration of the project.*

## Project Progress Photos



*Internal courtyard works underway*



# TWO WEEK LOOK AHEAD



*Temporary bridge installation underway*



*Grease Arrester installation completed*



*Installation of posts for perimeter fencing*



*Installation of steel for façade screen continues*



*Concrete poured for curved overhang slab*



*Stair 1 installation underway*
