




TWO WEEK LOOK AHEAD

PROJECT NAME: **Modernising Belconnen High**
 ADDRESS: **111 Murrانji Street, Hawker, ACT**
 DATE: **15/09/2017**

Note: The 'Two Week Look-ahead' provides a general overview of Cockram Construction's scheduled works over the next two weeks. The dates provided are anticipated dates and are subject to change without notification.

BELCONNEN HIGH DIRECTLY IMPACTED WORKS

Outside of the regular construction traffic, a crane will be on site on Monday, 18th September to lift in the temporary administration building on the eastern side. Dates and times for further craneage works will be confirmed prior to any further deliveries occurring.

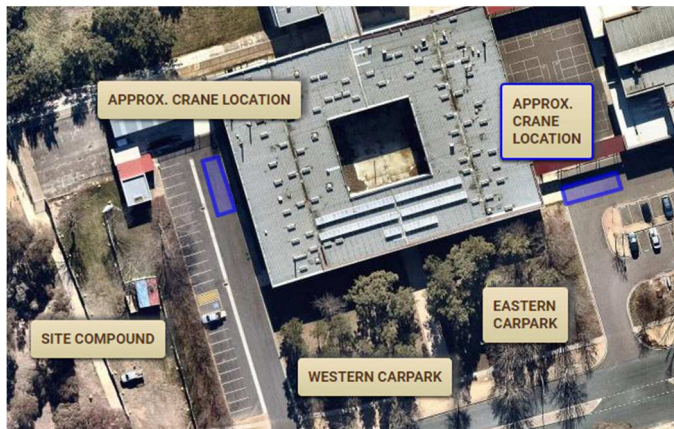

WORKS UPDATE

Roof works continuing as per schedule with the perimeter roof scaffold now removed and perimeter flashing continuing. The first stage of internal works will begin in the last week of September with CCA taking possession from the 23/09/17.



Progress photo of scaffold removed and parapet ready for flashing.

SITE TRAFFIC MANAGEMENT 15/09 – 29/09

Traffic management and Cockram supervision will be required for crane setup and associated deliveries. This will be in place during the site shed delivery on 18/09/17. Further traffic management to continue as per the Temporary Traffic Management Plan.

SITE ACCESS 15/09 – 29/09

ALL VISITORS MUST REPORT TO THE SITE OFFICE PRIOR TO ENTERING ANY OF THE CONSTRUCTION SITE.

- All contractors must park within the CCA site compound accessed off Murrانji Street.
- All workers must report and sign in at the CCA site compound to prior to starting work on site.
- Roof access is via the scaffold on the western side of the main building.
- Courtyard entry via temporary fence/gate in undercroft of main building.

OFF SITE 15/09 – 29/09

CCA continues with the procurement of trades for the project, as well as working in collaboration with EDU and consultants to finalise design elements. Notably the structural design continues for the central courtyard and refurbished structure.

MAIN BUILDING WORKS 15/09 – 29/09

Temporary administration building will be in place from the 18th of September and CCA will take possession of the first stage of internal works from the 23rd of the same month. From the 23/09/17 to the end of September, CCA will begin site establishment, services decommissioning and minor demolition works.

ROOF WORKS 15/09 – 29/09

Roofers will be continuing works to the main roof including:

- New under flashings are being installed.
- Permanent roof safety anchor system is installed and the temporary handrails have been removed.
- Locations of roof works as agreed with school. Construction work is being coordinated to minimise disturbance to school operation.

SERVICES 15/09 – 29/09

Existing roof mounted services are being managed to maintain functions that are required for day-to-day operations within the school.

NOTES:

1. Works scheduled above are a guide only and may be subject to change without notice due to a number of unforeseen events or circumstances. Cockram Construction will employ all reasonable measures to reduce disturbance to the school and neighboring residents in line with the Cockram Project Environmental Management Plan (PEMP).
2. Working times will vary and should be expected between the hours of **6.00am – 6.00pm Monday to Saturday.**
3. Heavy vehicles will be entering the site via Murrانji Street for the duration of the project. This is expected to increase progressively over the coming months and will increase site noise.
4. All traffic on site will follow the traffic management plan to ensure Belconnen High traffic can continue to move without interruptions.
