




TWO WEEK LOOK AHEAD

Project: **Modernising Belconnen High School**
 Address: **111 Murrnaji Street, Hawker, ACT**
 Date: **22/06/2018 – 06/07/2018**

Note: *The Two Week Look-ahead' provides a general overview of Cockram Construction's scheduled works over the next two weeks. The dates provided are anticipated dates and are subject to change without notification.*

Belconnen High Directly Impacted Works

The school can continue to be accessed via the western side of the building (as noted below) or by the gate next to the canteen. CCA will continue to coordinate works with the school.

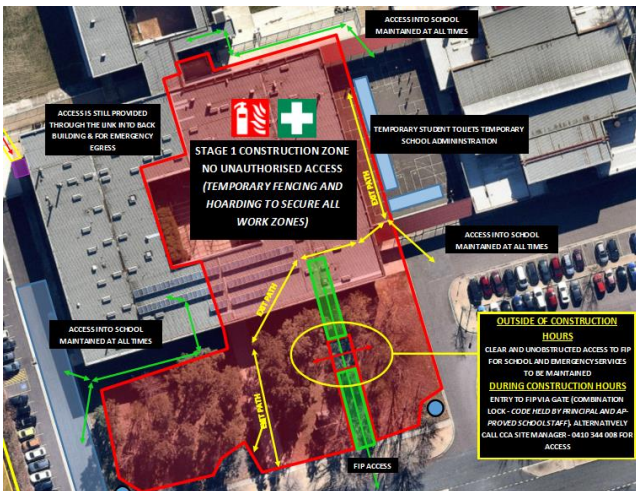

Works Update 22/06/18 – 06/07/18

Stage 1 construction works is now at the final phase. Window frames are all installed to the Ground Floor external walls with glazing to be finished in the next week. Vinyl and tiling to wet areas is complete on Level 1 with Ground Floor underway. Painting and carpet tiles continue to both floor levels.

Concrete footpath works to the eastern and southern elevations will be completed in the coming days. Form and steelwork for the new internal stair and infill slab is ongoing and will be poured late in the week ending 29th June. Joinery and furniture for Stage 1 are currently being delivered and installed as rooms are nearing completion.

Services 22/06/18 – 06/07/18

Isolation and relocation of services within Stage 1 is now minimal. CCA and services contractors are working closely together to coordinate new installations whilst managing the existing services to maintain functions that are required for day-to-day operations within the school.

Services fit-off is ongoing to both floor levels and will continue in the coming week. Stage 1 commissioning and testing is underway for the services trades.

In ground stormwater & sewer services are now completed with downpipes to be fully plumbed in the next week.

Off-Site 22/06/18 – 06/07/18

To date, all program critical trades have been engaged including all services, fit out and structural subcontractors. The design is now completed with continual review and updates as the project progresses. CCA continues to work closely with EDU and the School to ensure the project is completed in line with the requirements of Belconnen High School.

Site Traffic Management 22/06/18 – 06/07/18

Traffic management and Cockram supervision is implemented for all construction traffic. Ongoing Traffic management will continue as per the Temporary Traffic Management Plan and will be used as required for all forthcoming deliveries.

Site Access 22/06/18 – 06/07/18

ALL VISITORS MUST REPORT TO THE SITE OFFICE PRIOR TO ENTERING ANY OF THE CONSTRUCTION SITE.

- All contractors must park within the CCA site compound accessed off Murrnaji Street or west of the school.
- All workers must report and sign in at the CCA site compound prior to starting work on site.
- Any persons requiring roof access are to report to CCA prior to works commencing.
- Construction site entry will be from Murrnaji Street.
- Security cameras are installed on site to ensure the security of materials and equipment. These will only be recording outside of school hours.

Important Considerations

1. Works scheduled above are a guide only and may be subject to change without notice due to a number of unforeseen events or circumstances. Cockram Construction will employ all reasonable measures to reduce disturbance to the school and neighboring residents.
2. Working times will vary and should be expected between the hours of 6.00am – 6.00pm Monday to Saturday.
3. Heavy vehicles will be entering the site via Murrnaji Street for the duration of the project.

Project Progress Photos



Joinery and furniture installation underway.
